

Work Order ID 145262

Thursday, May 05, 2016 9:25:18 AM

145262

Page 1

Item ID: D6101-001

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Saddle Billet

Start Date: 5/6/2016 Start Qty: 40.00

40

Cust Item ID:

Required Date: 5/20/2016 Req'd Qty: 40.00

40

Customer:

Reference:

Approvals: Process Plan: MCS Date: MAY 05 2016

Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D6101	Rev B

100

0.00

100

PURCHASING

Purchasing

Memo

0.00

Purchasing

Issue P/O: 32296

a) Description: Aluminum billet

b) 6.00" x 6.250" x 2.00" thick

c) Tolerance on length are +0.030"/-0.000" $\pm$ 0.008"

d) Grain direction along 6.00" length

e) Material: 7075-T7351 (QQ-A-250/12)

f) Material certification required

40MAY 09 2016DAS
13
9-89

110

Receive & Inspect for Damage & Mat'l Certs

0.00

110

Packaging

Memo

0.80

Packaging

Ensure material certification is attached

40x SP/6-05-20

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QS1042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : _____									

Work Order ID 145262

Thursday, May 05, 2016 9:25:18 AM

145262

Page 2

Item ID: D6101-001

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Saddle Billet

Start Date: 5/6/2016 Start Qty: 40.00

40

Cust Item ID:

Required Date: 5/20/2016 Req'd Qty: 40.00

40

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC6- Inspect dimensions to drawing	0.00				40	0		DAS 14 9-33 16/05/24
120									
QC	Memo	0.00							
Quality Control	Ensure Material certification comply to Dwg D								
130	Identify as per dwg & Stock Location: MAT042	0.00				40	0		DAS 14 9-33 16/05/24
130									
Packaging	Memo	0.40							
Packaging	LOCATION: MAT042								
140	QC21- Final Inspection - Work Order Release	0.00							16/5/25 JF
140									
QC	Memo	4.00							
Quality Control									

MAY 24 2016

MCS

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY							
Environment ☐	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong
Design ☐	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions
Doc/Data ☐	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance
Equip/Tooling ☐	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect
Handling/Pre ☐	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing
Material ☐	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved
Internal Transport ☐	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing
Tribal Knowledge ☐	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish
LOA ☐	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread
Substation ☐	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence
Past Expiry Date ☐	☐	Manufacturing Process	OTHER :							
Misidentified ☐	☐	Past Due								

Picklist Print

Thursday, May 05, 2016 9:25:23 AM

Page 1

Work Order ID: 145262

145262

Parent Item: D6101-001

D6101-001

Parent Item Name: Saddle Billet

Start Date: 5/6/2016

Required Date: 5/20/2016

Start Qty: 40.00

Required Qty: 40.00

Comments: IPP B: 01.05.04New IssueEC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D6101-001P		Purchased	No			110	Each	0.0000	1	40			
D6101-001P									**				
7075-T7351 2X6X6.25													

40x SP/6-05-20

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause				FAULT CATEGORY			
Environment ☐	☐ No Re-verification	☐ Pressure/Forced	☐ Temperature/Cure	☐ Power Loss/Surge	☐ Positioned Wrong		
Design ☐	☐ Operator	☐ Bending	☐ Set-up	☐ Folio/Program	☐ Outside Dimensions		
Doc/Data ☐	☐ Offset/Setup	☐ Centre Not Concentric	☐ BOM/Route	☐ Grain	☐ Over/Under tolerance		
Equip/Tooling ☐	☐ Supplier	☐ Cracks	☐ Broken/Damage/Defect	☐ Weld	☐ Part Incorrect		
Handling/Pre ☐	☐ Training	☐ Crimp/Kink/Ripple/Wave	☐ Inspection Incomplete/Unqualified	☐ Wrong Stock Pulled	☐ Part Lost/Missing		
Material ☐	☐ Use for Testing	☐ Cuffs	☐ Contamination	☐ Out of Sequence	☐ Part Moved		
Internal Transport ☐	☐ Poor Information	☐ Crushing	☐ Countersink	☐ Off-set	☐ Drawing		
Tribal Knowledge ☐	☐ Rushing	☐ Heat Treat	☐ Cut Too Short	☐ Mislabeled	☐ Finish		
LOA ☐	☐ Product Improvement	☐ Wave/Twist in Tube	☐ Instructions Incomplete/Unclear	☐ Fit/Function	☐ Misread		
Substation ☐	☐ Process Improvement	☐ Marks/Chatter	☐ Drill Holes	☐ Misaligned/off center	☐ Turning Sequence		
Past Expiry Date ☐	☐ Manufacturing Process	OTHER : _____					
Misidentified ☐	☐ Past Due						

SPECIFICATION CONTROL DRAWING

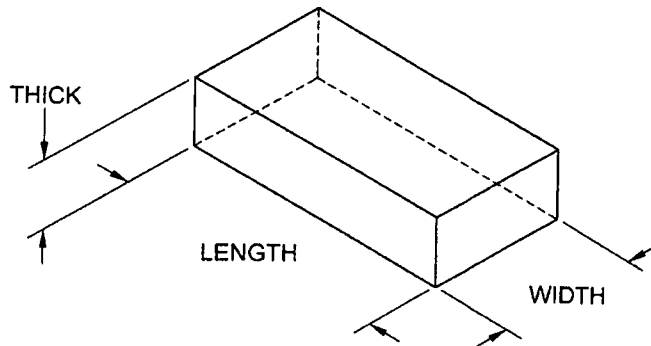

PURCHASE MATERIAL ACCORDING TO THE FOLLOWING TABLE. SPECIFY ALLOY, LENGTH x WIDTH x THICK (+0.030/-0.000), AND GRAIN DIRECTION AS SHOWN.

TOLERANCES ON ALL DIMENSIONS ARE +0.030/-0.000.

ALL DIMENSIONS ARE IN INCHES.

B ACCEPTABLE SPECIFICATIONS FOR 7075-T7351 ALUMINUM ARE AMS-QQ-A-250/12, QQ-A-250/12, OR ASTM B209

Part No.	Alloy	Length	Width	Thick	Grain Direction
D6101-001	7075-T7351 (QQ-A-250/12)	6.000	6.250	2.000	Along 6.000 Length
D6101-003	7075-T7351 (QQ-A-250/12)	7.875	6.250	2.000	Along 7.875 Length
D6101-005	7075-T7351 (QQ-A-250/12)	5.000	8.250	2.500	Along 5.000 Length
D6101-007	7075-T7351 (QQ-A-250/12)	7.750	8.250	2.500	Along 7.750 Length
D6101-009	7075-T7351 (QQ-A-250/12)	8.700	8.250	2.500	Along 8.700 Length
D6101-011	7075-T7351 (QQ-A-250/12)	9.700	8.250	2.500	Along 9.700 Length
D6101-013	7075-T7351 (QQ-A-250/12)	10.100	8.250	2.500	Along 10.10 Length
D6101-015	7075-T7351 (QQ-A-250/12)	9.450	6.250	2.500	Along 9.450 Length
D6101-017	7075-T7351 (QQ-A-250/12)	6.350	6.250	2.250	Along 6.350 Length

RELEASED
09/07/15/W

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 145262 MJS
16-05-05

B	ADDED D6101-015/-017, ADD ASTM B209	RF	09.04.23
A	NEW ISSUE	CP	01.03.30
REV.	DESCRIPTION	BY	DATE
DESIGN	CP	DART AEROSPACE LTD	
DRAWN	RF	HAWKESBURY, ONTARIO, CANADA	
CHECKED	<i>[Signature]</i>	DRAWING NO.	REV. B
MFG. APPR.	<i>[Signature]</i>	D6101	SHEET 1 OF 1
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	<i>[Signature]</i>	SADDLE BILLET, 7075	NTS
DATE	09.04.23	COPYRIGHT © 2001 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER

Purchase Order ID PO32296

Purchase Order Date 5/9/2016
PO Print Date 5/9/2016

Page Number 1 of 3

Order From :

METAUX CASTLE
P.O. BOX 4090 STN A
TORONTO, ONTARIO M5W OE9
CANADA

VU-MET002

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

E-MAILED

Contact Name
Vendor Phone

Ship To Contact

Ship To Phone

Ship Via:

Yours ppd

Ship Acct:

Buyer
Customer POID
Customer Tax #
Terms
Currency
FOB

Chantal Lavoie

10127-2607
Net 30
USD

Destination-Collect

MAY 09 2016

Line Nbr	Reference Vendor Part Number Line Comments Delivery Comments	Description/ Mfg ID	Req Date/ Taxable Promise Date	CD	Req Qty/ Unit of Measure	PO Unit Price	Extended Price
1	D6101-001P ✓	7075-T7351 2X6X6.25	5/24/2016 Yes 5/24/2016		40.00 Each	\$26.88	\$1,075.20

AS PER DWG D6101 REV. B
B145262
SIZE: 6.00" X 6.250" X 2.00" THICK
GRAIN DIRECTION ALONG 6.00" LENGHT
MATERIAL: 7075-T7351 QQ-A-250/12
TOLERANCE AS PER QUOTE +.030"/-.000"

8/6-05-20

Line Total: \$1,075.20

2	D6101-003P	7075-T7351 2X6.25X7.875	5/24/2016 Yes 5/24/2016		20.00 Each	\$35.29	\$705.80
---	------------	-------------------------	-------------------------------	--	---------------	---------	----------

AS PER DWG D6101 REV. B
B145263
SIZE: 7.875" X 6.250" X 2.00" THICK
GRAIN DIRECTION ALONG 7.875" LENGHT
MATERIAL: 7075-T7351 QQ-A-250/12
TOLERANCE AS PER QUOTE +.030"/-.000"

8/6-05-20

Note:

5/9/2016

**Castle Metals®**

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 1 of 2

Shipment No:2978240

Ship From: A. M. CASTLE & CO. 2150 ARGENTIA ROAD MISSISSAUGA, ON L5N 2K7 CAN		Sold To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA		Ship To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CAN		Deliver To: DART AEROSPACE LTD 1270 ABERDEEN HAWKESBURY, ON K6A 1K7 CA	
Date Shipped	F.O.B.	Freight Terms		Carrier		BOL No	
19-MAY-16	ORIGIN	Prepaid		MANITOULIN		2978240-2	

Shipment Details	Final Destination Branch - TOR
-------------------------	---------------------------------------

Order No 4354705	Line No 1	Item No 752237!MO	Description 2.0000.PL.7075.T7351.ALUMINUM.US1.48.5000.144.5000 CUT RECTANGLE TO 6.25 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 6")) X 6 IN (+ .0310/- .0000 IN (GRAIN TO RUN ALONG 6")) - ALUMINUM PLATE SAW SPECIFICATIONS: AMS-QQ-A-250/12				
Purchase Order No 32296		Part Number YOUR ITEM NUMBER: D6101-001		Ordered Qty 40.00 PCS		Invoice Qty 40.00 PCS	
Details		ALL PAPERWORK MUST FOLLOW ORDER / CUSTOMER MUST RECEIVE AT TIME OF DELIVERY ALL MATERIAL MUST HAVE IDENTIFYING MARKINGS EX:HEAT #S Email P/s and certs to: clavoie@dartaero.com END USER: DART AEROSPACE END USE: COMMERCIAL AIRCRAFT PARTS					
Delivery No. 120431545	Mill KAISER ALUMINUM	Heat Number 	Mech Id	PCS 40	Width (IN)	Length (IN)	Shipped Qty(LBS) 309.6638

These commodities/technologies are subject to US Export Administration & US State Dept. Regulations and, if intended for export, were/are exported thereunder. Diversion contrary to US Law is Prohibited.

We hereby certify the material covered by this certification conforms in accordance with the above specifications and has been found to meet the applicable requirements for the material, including any specifications forming a part of the description. Test reports are on file subject to examination. All claims for defective material are waived unless made in writing to A.M. Castle & Co. within 60 days of the shipment. Material cut to the correct size, or material cut by the customer cannot be returned

These commodities, technology or software were exported from the United States in accordance with the Export Administration Regulations. Diversion contrary to US law prohibited.

Date Printed: 19-MAY-2016 05:51:29 PM



Castle Metals®

A. M. Castle & Co.

PACKING SLIP/
CERTIFICATE OF CONFORMANCE

Page 2 of 2

for credit.	
Reviewed by Authorized Castle Metals Representative:	Date: Name:

Chris Gher

MAY 19 2016



SHIP TO:

A M CASTLE METALS
4175 ROYAL DRIVE, SUITE 600
KENNESAW, GA 30144

SOLD TO:

AM CASTLE & CO- SOLD TO
1420 KENSINGTON RD
SUITE 220
OAK BROOK, IL 60523

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number

4409242

CUSTOMER PO NUMBER: 350906		WORK PACKAGE:		CUSTOMER PART NUMBER: 752237		SHIP RUN/LOAD: 103484/16		GOV'T CONTRACT NUMBER:	
KAISER ORDER NO: 1201307	LINE ITEM: 1	SHIP DATE: 25-FEB-2016	ALLOY: 7075	CLAD: BARE	TEMPER: T7351	PRODUCT DESCRIPTION: KaiserSelect Plate			
WEIGHT SHIPPED: 7234 LB	QUANTITY: 5 PCS EST.	TRUCK B/L #: 2058844	GAUGE: 2.0000 IN (50.8000 MM)		DIAMETER/WIDTH: 48.500 IN (1231.9 MM)		LENGTH: 144.500 IN (3670.3 MM)		

MHU 1975316: LOT 16855787: 2 pieces;

MHU 1978130: LOT 784295A8: 2 pieces;

MHU 1978219: LOT 784509A2: 1 pieces;

DAS

14

9-89

16/05/24

Certified Specifications

AMS 4078/RevJ
ASTM B 209/Rev14
BSS 7055/RevB
DPS 4.713/RevAK
MMS 159/RevT

AMS-QQ-A-250/12/RevA
ASTM B 594/Rev13
CMMP 025/RevU
GAMPS 9101/RevB/AmdSCN1
PS 21211/RevP

AMS-STD-2154/RevA
BAC 5439/RevJ
CSTI 006/RevE
GSS16100/RevG/Amd1

Test Code: 4297

Test Results

Lot: 16855787 Cast 140

Drop 32

Ingot 4

Melted in USA

(ASTM E8/B557)

(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	74.0 : 74.2 (510 : 512)	63.3 : 63.7 (436 : 439)	12.6 : 12.8

(ASTM E1004)

(EN 2004-1)

Conductivity %IACS :	40.4 Min	40.5 Max
(MS/M) :	23.4 Min	23.5 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.05	0.15	1.5	0.02	2.5	0.20	5.9	0.03	0.01	0.01	TOT 0.05

MAR 02 2016





Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4409242

Lot: 784295A8 Cast 140 Drop 28 Ingot 4 Parent Lot: 167692B3 Melted in USA

(ASTM E8/B557)

(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	72.6 : 72.8 (501 : 502)	62.1 : 62.2 (428 : 429)	12.4 : 12.5

(ASTM E1004)

(EN 2004-1)

Conductivity %IACS :	40.9 Min	41.1 Max
(MS/M) :	23.7 Min	23.8 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.07	0.18	1.4	0.02	2.5	0.20	5.8	0.03	0.01	0.01	TOT 0.05

Lot: 784509A2 Cast 140 Drop 38 Ingot 3 Parent Lot: 168665B8 Melted in USA

(ASTM E8/B557)

(EN 2002-1)

Tensile:	Temper	Dir / # Tests	Ultimate KSI (MPA)	Yield KSI (MPA)	Elongation %
	T7351	LT / 2 (Min:Max)	73.9 : 74.6 (510 : 514)	63.1 : 64.4 (435 : 444)	12.1 : 12.3

(ASTM E1004)

(EN 2004-1)

Conductivity %IACS :	40.7 Min	40.7 Max
(MS/M) :	23.6 Min	23.6 Max

(ASTM E1251)

Chemistry:	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER
Actual(wt%)	0.06	0.15	1.5	0.01	2.5	0.22	5.6	0.02	0.01	0.01	TOT 0.05

KAISER ALUMINUM

Trentwood Works - Spokane, WA 99215
Phone: (800) 367-2586

CERTIFIED TEST REPORT

Serial Number
4409242

ALLOY LIMITS

	SI	FE	CU	MN	MG	CR	ZN	TI	V	ZR	OTHER	MAX
7075												
MIN(wt%)	0.00	0.00	1.2	0.00	2.1	0.18	5.1	0.00	0.00	0.00	EACH	0.05
MAX(wt%)	0.40	0.50	2.0	0.30	2.9	0.28	6.1	0.20	0.05	0.05	TOT	0.15

Aluminum Remainder

ORDER COMMENTS

AMC CA-15413A R 7
AMS 4078,AMS QQ-A-250/12,AMS STD-2154,A
STM B209,ASTM B594,BS
S 7055,CMMP 025,CSTI 006,DPS 4.713,GAMP
S 9101,MMS 159,PS 212


11

TEST NOTES

Metel represented by this test report was 100% Type I
(immersion) ultrasonically tested from one side with 3mm
dead zones top and bottom and meets the Class A and Class B
requirements of all specifications referenced on this test
report. No surface marking of sonic indications is
performed.

CERTIFICATION

Kaiser Aluminum Fabricated Products, LLC (Kaiser), is ISO 9001:2008/AS9100C certified and hereby certifies that all material shipped under this order:
* has been inspected, tested, and found to be in conformance with the requirements of the specifications indicated herein. For material thicknesses outside specification limits, mechanical properties are as shown herein and chemical composition meets specification requirements.
* was melted in the United States of America or a qualifying country per DFARS 225.872-1(a), was manufactured in the United States of America, and meets the requirements of DFARS 252.225 for domestic content.
* has been thermally processed in compliance with AMS 2772, where applicable.
* is mercury free, within the limits of detection of ASTM E1251 (< 1 ppm).
* is in compliance with RoHS 2, European Union Directive 2011/65/EU.
* is in compliance with and regularly monitors any updates to the European Chemical Agency, ECHA, REACH regulations, (EC) n°1807/2006.
* is free of Conflict Minerals, as defined in Section 15.2 of the Dodd-Frank Act.
Any warranty is limited to that shown on Kaiser Aluminum's standard general terms and conditions of sale. Test reports are on file, subject to examination. Test reports shall not be reproduced except in full, without the written approval of the Kaiser Aluminum laboratory. The recording of false, fictitious or fraudulent statements or entries on the certificate may be punished as a felony under federal law.



JAMES HEMENWAY, TECHNICAL PROCESS MANAGER

